INDIVIDUAL GANTT CHART

PROJECT TITLE	**SLAMDAM**
PROJECT MANAGER	Omar Saleh
COMPANY NAME	Zephyr Consulting Limited
COUNTRY OF DEPLOYMI	Pakistan
THEMATIC AREA	Resilient Infrastructure
DATE	**20 Dec - 31 Jul**

TASK ID	Milestones (With Each Monthly Deliverable)	Person Responsible	START DATE	DUE DATE	Task Status
	TITLE				
	Phase 1; project inception				
	MS 1: project Kick off		Dec	Jan	
	MS 2: Inception report		Dec	Jan	
	phase 2: Flood risk assessment			Jan	
	MS3: Flood risk assessment		Jan	Feb	
	MS4: Location confirmation		Jan	Feb	
	phase 3: Monitoring and evaluation				
	MS 5: M & E plan (including benefits mechanism)		Jan	Feb	
	Phase 4: SLAMDAM development and shipment				
	MS6: Manufacture SLAMDAM		Feb	Mar	
	MS7: Locally stored SLAMDAM		Mar	Apr	
	Phase 5: training and demonstration				
	MS8: Trained people		Mar	Apr	
	MS9: Dry run demonstration		Mar	Apr	
	MS10: Real life demonstration		Mar	Apr	
	Phase 6: roadmap and project closure				
	MS11: Final M$E report		Apr	June	
	MS12: Final roadmap		May	Jul	
	MS13: Project closure report		Jun	Jul	

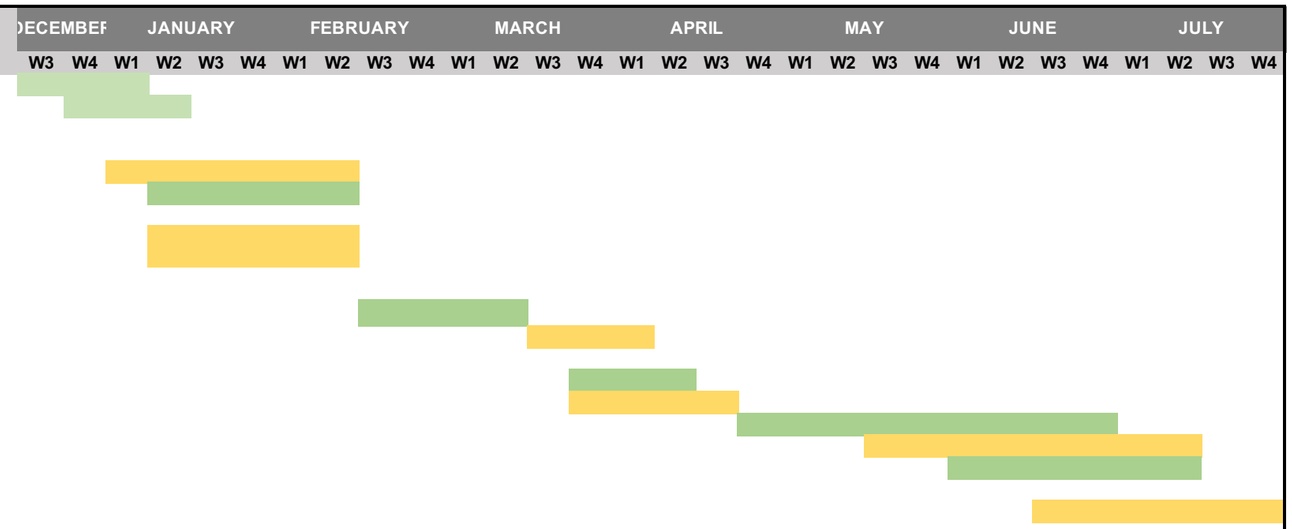

Outputs

Output 1- inception meeting and report	Jan	
Output 2- report on completion of Flood risk assessment (including Hydro	Mid Feb	
Output 3- rreport on completion of manufactured flood barrier and detailed	5-Mar	
Output 4- project closure report	Jul	

The intended key project outcomes are;

1 Resilience to floods is strengthened
2 Capabilities to manage risk of floods is
3 Mechanism in place to ensure a learning curve

Dissemination and Information Sharing Deliverables

1 Risk assessment document including flood data global data sets; area data week; field visit report; data portal (week 4 -6)
2 Project team presentations
3 Training materials on how to use SLAMDAM (Week 11)
4 Story Map (Week 27)
5 Pitures/videos of deployment of flood barrier (week 25)
